

Wembdon St Georges Primary School

Classroom Extension Project

Newsletter

Welcome to our newsletter which we hope will keep you informed of the activities at the school.
Please feel free to contact me on [07789 397401](tel:07789397401) should you have any queries.

The Construction Team



Warren Robinson
Site Manager



Terry Scull
Quantity Surveyor



Andrew Moss
Construction Manager



Matt Casey
D&B Manager



Steve Bass
SHE Manager

The Project:

The project is a 2-storey extension to the existing school to provide much needed extra classroom space, and internal staircase and lift along with improved ancillary rooms and circulation space.

Our aim is to carry out and complete the project with as little impact on the school, pupils and residents as possible, and are due to have the extension ready for the new school term in September 2015.

What have we done?

The blockwork to the main building ground to first is complete, and the pre-cast concrete planks have been installed to the first floor.


We have removed the old roof to the existing building, in readiness for our connection works and single storey extension to this part.

We are coordinating our internal works in the school over the Easter Break so that we do not affect the school's day to day operations.

We have also been planning and completing the design of the roof trusses ready for the planned installation in early May.



The First Floor

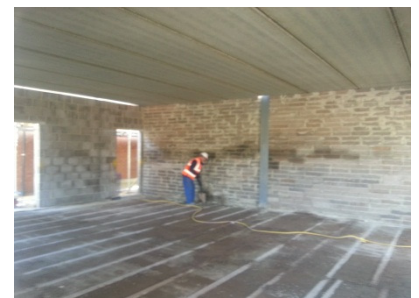

One of the new Classrooms



The Steel Frame for the new glazing to the staircase.



Roof removed from the existing school extension

Apologies:

We would like to apologize for any inconvenience caused when we accidentally set off the intruder alarm to the school on the Morning of 26th March 2015. We hope it didn't affect anyone too much.

The Next Month?

This month the building really starts to take shape with the new floor and walls to the single storey extension being constructed.

The block walls to the new build extension will also be built readying ourselves for the new roof in early May.

We will be finalizing the design to enable us to start the internal works in Mid May.

Deliveries:

We will always plan to have deliveries outside of the busy periods, but there can always be a "rogue" lorry/van arrive. If this does happen the school and residents will always take priority and we will try to keep any disruption to a minimum.

If anything does cause anyone issues, please feel free to contact us the numbers below.

Considerate Constructors:

All Kier projects are registered with the Considerate Constructors Scheme.

This is a scheme that promotes reducing the impact of construction sites on the local community and surrounding area. As part of the process, we would welcome any comments you may have-please contact the Site Manager Warren Robinson on 07789 397401. Alternatively you may wish to call the scheme hotline on 0800 783 1423 if you do not wish to speak to us direct.



If you have any comments/suggestions, please feel free to contact me on the mobile number above or via email:
warren.robinson@kier.co.uk

If you wish to receive this newsletter by email in the future please email me at warren.robinson@kier.co.uk
